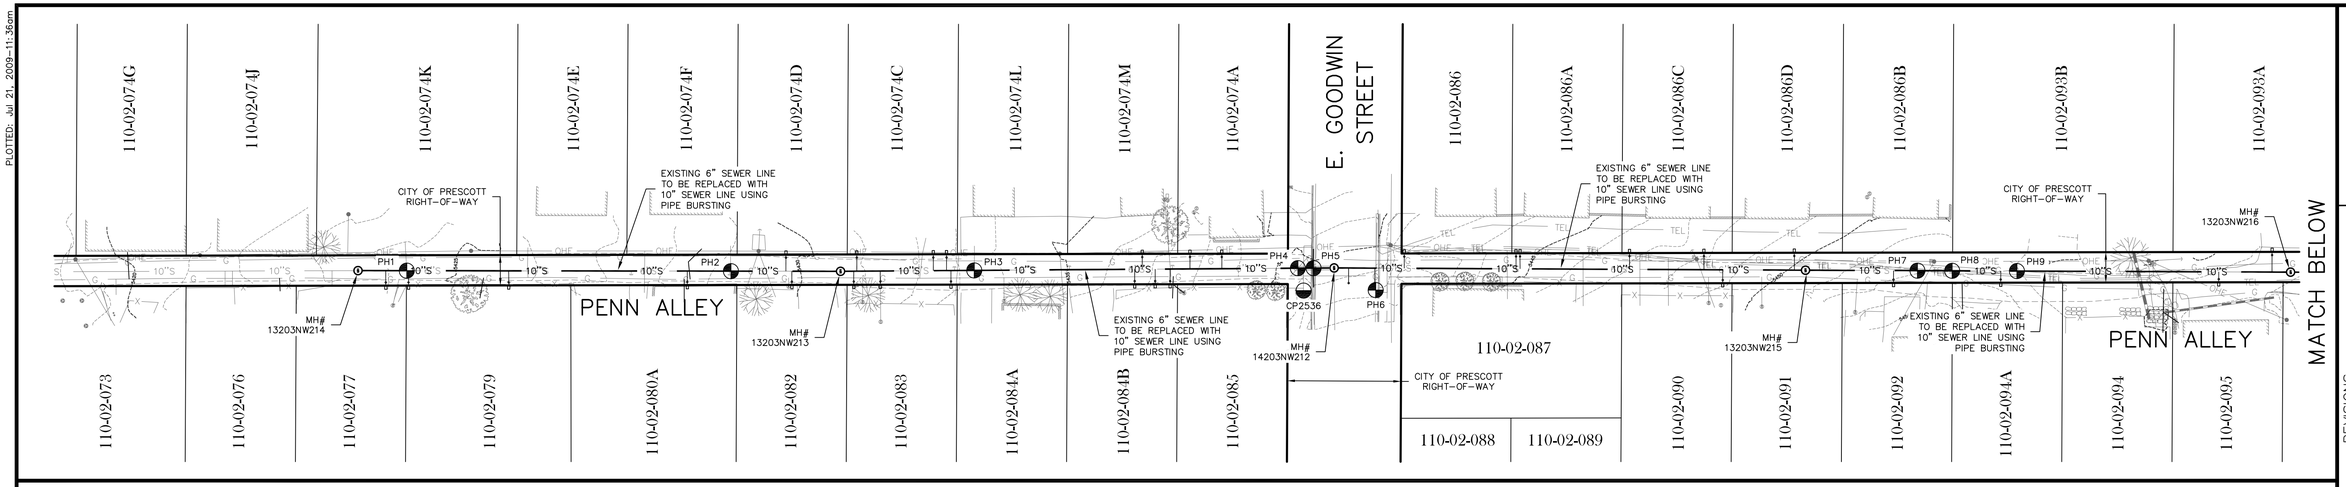

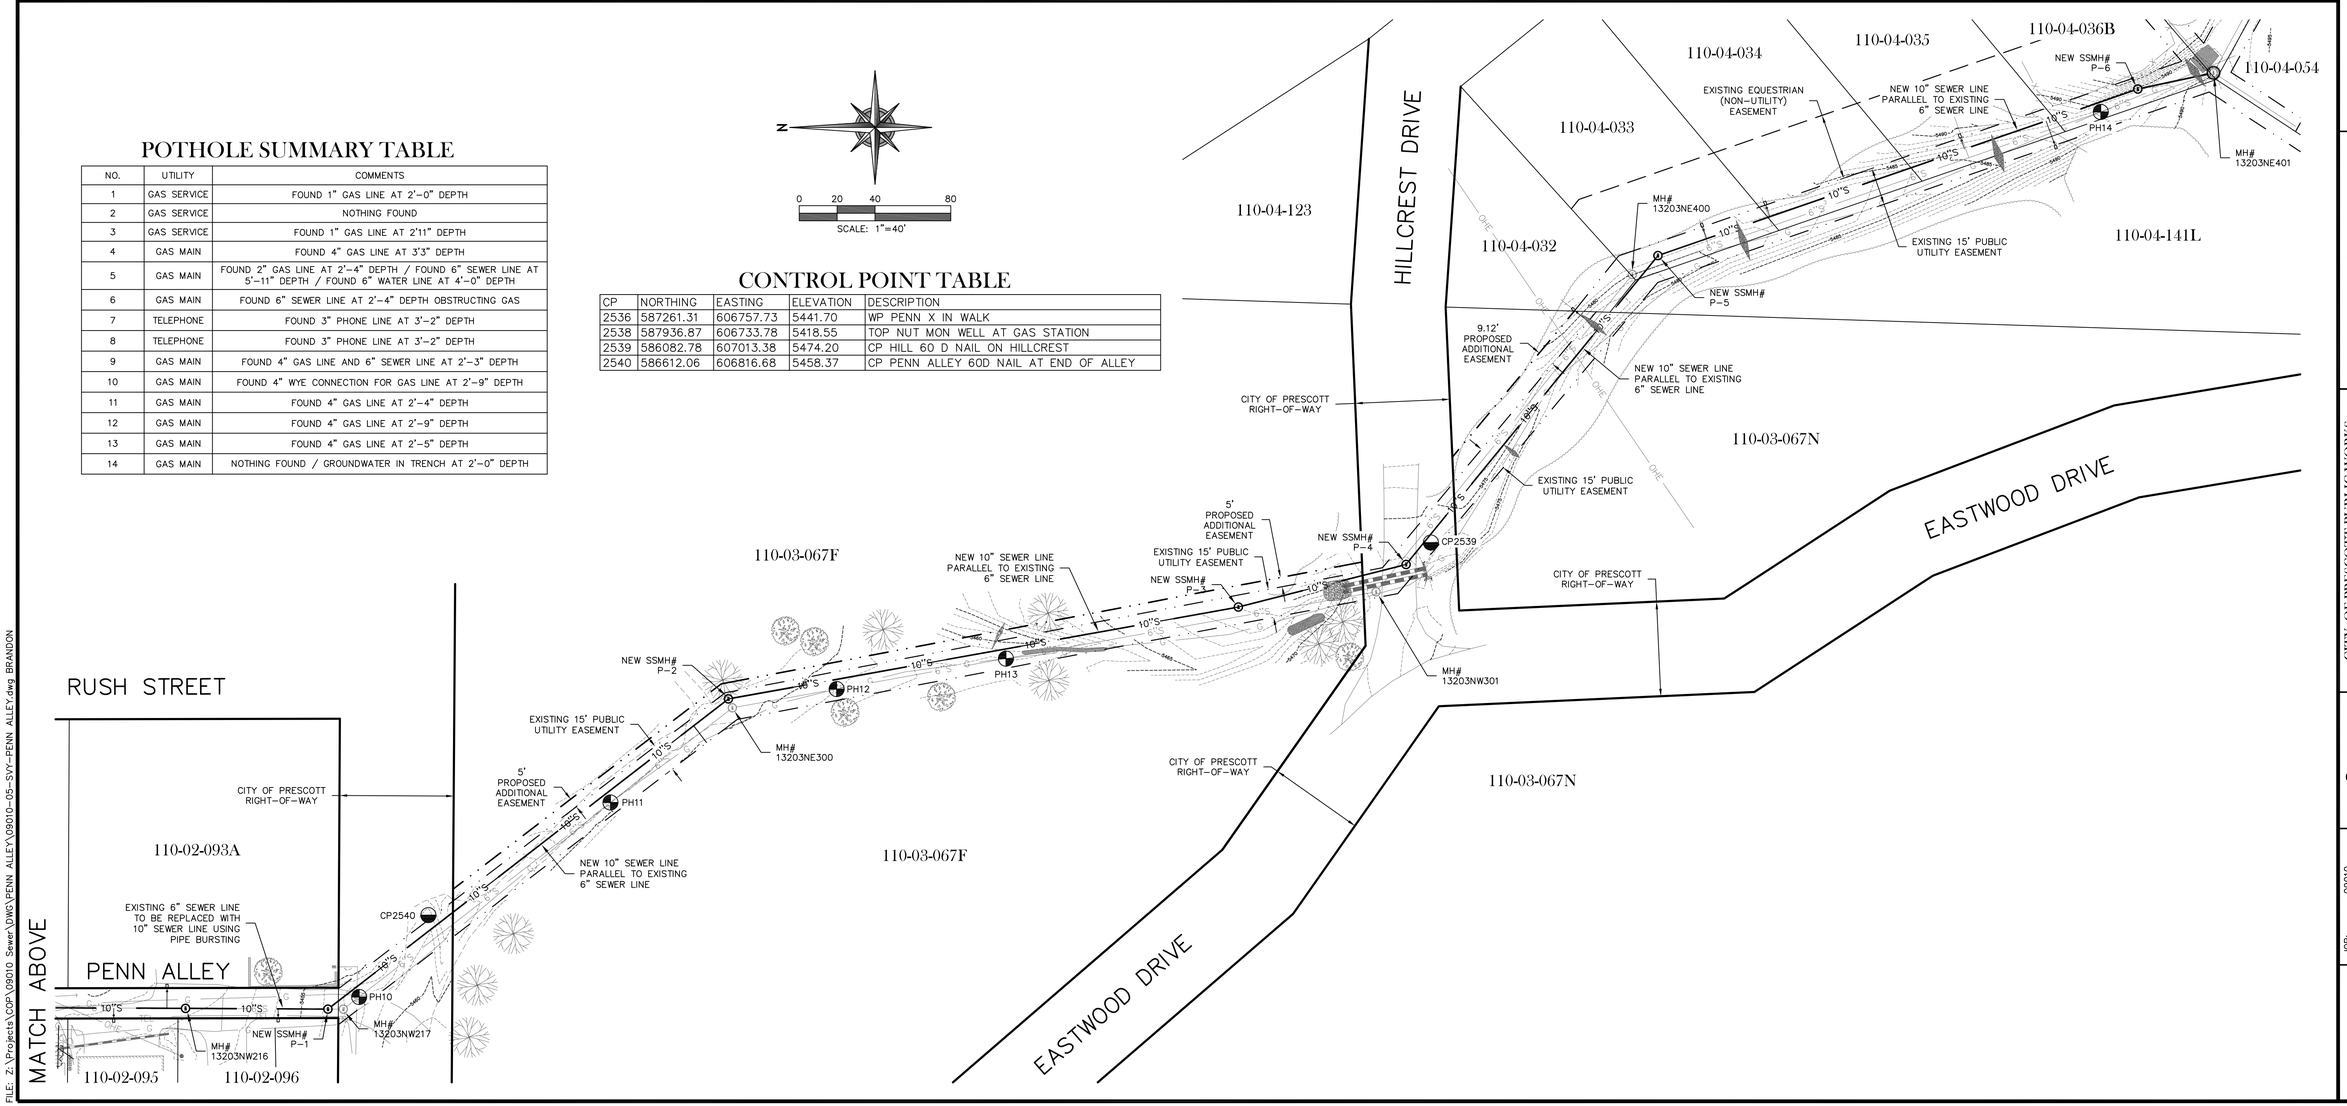

POTHOLE SUMMARY TABLE

NO.	UTILITY	COMMENTS
1	GAS SERVICE	FOUND 1" GAS LINE AT 2'-0" DEPTH
2	GAS SERVICE	NOTHING FOUND
3	GAS SERVICE	FOUND 1" GAS LINE AT 2'11" DEPTH
4	GAS MAIN	FOUND 4" GAS LINE AT 3'3" DEPTH
5	GAS MAIN	FOUND 2" GAS LINE AT 2'-4" DEPTH / FOUND 6" SEWER LINE AT 5'-11" DEPTH / FOUND 6" WATER LINE AT 4'-0" DEPTH
6	GAS MAIN	FOUND 6" SEWER LINE AT 2'-4" DEPTH OBSTRUCTING GAS
7	TELEPHONE	FOUND 3" PHONE LINE AT 3'-2" DEPTH
8	TELEPHONE	FOUND 3" PHONE LINE AT 3'-2" DEPTH
9	GAS MAIN	FOUND 4" GAS LINE AND 6" SEWER LINE AT 2'-3" DEPTH
10	GAS MAIN	FOUND 4" WYE CONNECTION FOR GAS LINE AT 2'-9" DEPTH
11	GAS MAIN	FOUND 4" GAS LINE AT 2'-4" DEPTH
12	GAS MAIN	FOUND 4" GAS LINE AT 2'-9" DEPTH
13	GAS MAIN	FOUND 4" GAS LINE AT 2'-5" DEPTH
14	GAS MAIN	NOTHING FOUND / GROUNDWATER IN TRENCH AT 2'-0" DEPTH

CONTROL POINT TABLE

CP	NORTHING	EASTING	ELEVATION	DESCRIPTION
2536	587261.31	606757.73	5441.70	WP PENN X IN WALK
2538	587936.87	606733.78	5418.55	TOP NUT MON WELL AT GAS STATION
2539	586082.78	607013.38	5474.20	CP HILL 60 D NAIL ON HILLCREST
2540	586612.06	606816.68	5458.37	CP PENN ALLEY 60D NAIL AT END OF ALLEY

CALL TWO WORKING DAYS BEFORE YOU DIG
1-800-STAKE-IT
1-800-782-5348
(OUTSIDE MARICOPA COUNTY)

REVISIONS

NUM.	DESCRIPTION	DATE	BY

GRANITE BASIN ENGINEERING, INC.
3605 Crossings Dr., Ste. B
Prescott, AZ 86305
928.717.0187
928.717.0181 fax

CITY OF PRESCOTT PUBLIC WORKS
433 NORTH VIRGINIA STREET
PRESCOTT AZ 86301
(928) 777-1130

CIP # S-13-02134 PENN ALLEY
SEWER REPLACEMENT PROJECT
PENN ALLEY REPLACEMENT
PROJECT SUMMARY MAP

PRELIMINARY
NOT FOR
CONSTRUCTION

JOB:	09010
DATE:	JULY 2009
SCALE:	AS SHOWN
DRAWN:	TS
DESIGNED:	DB
CHECKED:	DB

5

PLOTTED: Jul 21, 2009-11:36am
FILE: Z:\Projects\CCP\09010 Sewer\DWG\PENN ALLEY\09010-05-SVY-PENN ALLEY.dwg BRANDON
